


ID	Task Name	Duration	Start	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
1	4 RRFB's Winchester Street	3 days	Mon 3/27/23	Wed 3/29/23												
2	Phase 1 Traffic Pattern	1 day	Mon 3/27/23	Mon 3/27/23												
3	DEMO Remove Existing Sidewalk from (STA 112+00 RT) to (STA 117+00 RT) Test Pit (114+24 RT 20)	1 day	Mon 3/27/23	Mon 3/27/23												
4	DRAINAGE Install CB#34 (116+50 RT 19.8) Remove Existing MH Between CB#34-CB#32	1 day	Mon 3/27/23	Tue 3/28/23												
5	DRAINAGE Install 88LF of 24" HDPE from CB#34 (116+50 RT 19.8) to CB#32 (115+78 RT 45.2)	1 day	Tue 3/28/23	Tue 3/28/23												
6	DRAINAGE Install CB#32 (115+78 RT 45.2)	0.5 days	Tue 3/28/23	Tue 3/28/23												
7	DRAINAGE Install 117LF of 24" HDPE from CB#32 (115+78 RT 45.2) to CB#27 (114+25 RT 45.7) Install CB#27	2 days	Wed 3/29/23	Thu 3/30/23												
8	DRAINAGE Install 47LF of 8" SDR from CB#6 (200+90 RT 39.3) to MH#53 (201+33 RT 40.9) Install MH #53	1 day	Tue 3/28/23	Wed 3/29/23												
9	DEMO Remove Both Roadway Islands at Peal Street/Island Street Intersection Temp Pave	1 day	Wed 3/29/23	Thu 3/30/23												
10	DRAINAGE Install 81LF of 24" HDPE from CB#27 (114+25 RT 45.7) to CB#24 (113+50 RT 28)	1 day	Fri 3/31/23	Fri 3/31/23												
11	DRAINAGE Install APPROX 50LF of 24" HDPE from CB#27 (114+25 RT 45.7) to CL Road	1 day	Thu 3/30/23	Fri 3/31/23												
12	DRAINAGE Install CB#24 (113+50 RT 28)	0.5 days	Mon 4/3/23	Mon 4/3/23												
13	DRAINAGE Install 80LF of 24" HDPE from CB#24 (113+50 RT28) to CB#21 (112+69 RT 31)	1 day	Mon 4/3/23	Tue 4/4/23												
14	DRAINAGE Install 32LF of 15" HDPE from CB#24 (113+50 RT 28) to CB#26 (113+50 LT 4) Install CB#26	1.5 days	Fri 3/31/23	Tue 4/4/23												
15	DRAINAGE Install CB#21 (112+69 RT 31)	0.5 days	Tue 4/4/23	Tue 4/4/23												
16	DRAINAGE Install 128LF of 24" HDPE from CB#21 (112+69 RT 31) to CB#50 (111+39 RT 31.4) Install CB#50	2 days	Wed 4/5/23	Thu 4/6/23												
17	DRAINAGE Install 31LF of 15" HDPE from CB#21 (112+69 RT 31) to CB#52 (112+69) Install 4LF of 15" HDPE to CB#23 (112+69 LT 4) Install CB# 52 and CB#23	1 day	Tue 4/4/23	Wed 4/5/23												
18	SEWER Install SMH#4 (109+70 RT 9.9)	1 day	Wed 4/5/23	Thu 4/6/23												
19	DRAINAGE Install 89LF of 24" HDPE from CB#50 (111+39 RT 31.4) to CB#18 (110+50 RT 31)	1 day	Fri 4/7/23	Fri 4/7/23												
20	DRAINAGE Install 31LF of 15" HDPE from CB#18 (110+50 RT 31) to CB#51 (110+50) Install 4LF of 15" HDPE to CB#20 (110+50 LT 4) Install CB#51 and CB#20	1 day	Mon 4/10/23	Mon 4/10/23												
21	DRAINAGE Remove Existing Structure #1670 Fill and Abandon Pipe 18.6 CY	1 day	Tue 4/11/23	Tue 4/11/23												
22	DRAINAGE Remove Existing Structure #1686 Fill and Abandon Pipe 14CY	1 day	Wed 4/12/23	Wed 4/12/23												
23	Remove Pavement Install Yard Hydrant Riverside Plaza Roundabout Grading	3 days	Thu 4/6/23	Tue 4/11/23												
24	DRAINAGE Remove Existing Structure #13332 Remove Existing Structure #12391 Fill and Abandon Pipe From #1686-#13332 and #13332-12391 21.8CY	2 days	Thu 4/13/23	Fri 4/14/23												
25	Box Cut Remaining Shoulder on Win. Right Side	3 days	Tue 4/11/23	Fri 4/14/23												
26	(Sub) N.E.S.S. Remove Temporary Traffic Lights From Win/Key Road Intersection	2 days	Fri 4/14/23	Tue 4/18/23												
27	New Traffic Pattern Switch Phase #3	1 day	Mon 4/17/23	Mon 4/17/23												
28	DRAINAGE Install 94LF of 24" HDPE from Outlet (117+50) to CB#34 (116+50 RT 19.8) DRAINAGE Remove Existing CB#2159 and Exting 30" RCP	3 days	Tue 4/18/23	Thu 4/20/23												
29	DRAINAGE Remove Existing Structures #12428, 12999, 13556, 1537, 1506, and 13638. Fill and Abandon Existing 15" RCP Remove 12" CMP 4.2CY	4 days	Fri 4/21/23	Wed 4/26/23												
30	DRAINAGE Install 31LF of 15" HDPE from CB#20 (110+50 LT 4) to CB#19 (110+37 LT 32) Install CB#19 Connect Existing 12"CMP to CB#19 Install Retaining Water Service to McDonalds	2 days	Thu 4/27/23	Fri 4/28/23												
31	DRAINAGE Install 27LF of 15" HDPE From CB#22 (112+69 LT 31) to CB#23 (112+69 LT 4) Install CB#22	1 day	Mon 5/1/23	Mon 5/1/23												
32	DRAINAGE Install 27LF of 15" HDPE from CB#25 (113+50 LT 31) to CB#26 (113+50 LT 4) Install CB#25	1 day	Tue 5/2/23	Tue 5/2/23												
33	SEWER Remove Existing Sewer Cleanout Install New SMH #5 (111+72 LT 34)	2 days	Wed 5/3/23	Thu 5/4/23												

Project: Keene, NH Winchester
Date: Wed 3/22/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
34	(Sub) Tri-State Curb Installing Riverside Plaza Roundabout Curb and Misc. Curb <i>STA 99+65 to 102+50 center island</i>	2 days	Tue 4/18/23	Wed 4/19/23												
35	Riverside Plaza Roundabout Grading	5 days	Thu 4/20/23	Wed 4/26/23												
36	CONSTRUCT Vegetation Treatment Swale	8 days	Thu 4/27/23	Mon 5/8/23												
37	(Sub) Tri-State Curb Flatwork Setup and Place Concrete <i>Riverside Plaza roundabout and STA 99+65 to 101+15</i>	6 days	Fri 4/21/23	Fri 4/28/23												
38	(Sub) N.E.S.S. Installing Light Bases and RRFB <i>on Winchester Street</i>	7 days	Mon 5/1/23	Tue 5/9/23												
39	SEWER Install New Sewer Main Truck Line From Existing SMH (400+55) to SMH#6 (115+15 LT 104)	4 days	Fri 5/5/23	Wed 5/10/23												
40	SEWER Install New SMH#6 (115+15 LT) Install New Service	2 days	Thu 5/11/23	Fri 5/12/23												
41	Island Street Closed to Pedestrians Bridge Work Begins	0 days	Mon 5/15/23	Mon 5/15/23												
42	E.D. Swett Bridge Demo	46 days	Mon 5/15/23	Wed 7/19/23												
43	SEWER Remove Existing Sewer Line Install New Services From SMH#6 (115+15 LT) to Corner of Island Street and Pearl Street	3 days	Mon 5/15/23	Wed 5/17/23												
44	DEMO Remove Existing Sidewalk at Corner of Pearl Street and Winchester Street	2 days	Thu 5/18/23	Fri 5/19/23												
45	WATER Install Install 12"x12" Tee Install 12" Gate Valve	1 day	Mon 5/22/23	Mon 5/22/23												
46	WATER Install 60LF of 12" Water Line from (114+00 LT 10)	2 days	Tue 5/23/23	Wed 5/24/23												
47	WATER Install 60LF of 12" Water Line on Island Street Install 12"x12"x8" Tee for Pearl Street Connection	2 days	Thu 5/25/23	Fri 5/26/23												
48	WATER Install 40LF of 12" Water Line on Island Street Install 12"x12"x8" Tee for Winchester Street Connection	2 days	Mon 5/29/23	Wed 5/31/23												
49	WATER Install 120LF of 12" Water Line on Island Street to (502+06 LT 14) Install 12" Gate Valve	4 days	Thu 6/1/23	Tue 6/6/23												
50	WATER Install 120LF of 8" Water Line on Pearl Street Install 8" Gate Valve	3 days	Wed 6/7/23	Fri 6/9/23												
51	(Sub) N.E.S.S. Street Light installation and RRFB Installation <i>on Winchester Street</i>	5 days	Mon 6/12/23	Fri 6/16/23												
52	Remove Existing Sidewalks and Curb Winchester Street <i>STA 101+50 to Key Rd.</i>	10 days	Tue 5/9/23	Mon 5/22/23												
53	(Sub) Tri-State Curb Granite Curb STA 101+50 to STA 108+50	5 days	Tue 5/16/23	Mon 5/22/23												
54	WATER Install 200LF of 8" Water Line on Winchester Street Install 8" Gate Valve	7 days	Mon 6/12/23	Tue 6/20/23												
55	Grading Sidewalks STA 101+50 to STA 108+50	15 days	Tue 5/23/23	Tue 6/13/23												
56	E.D. Swett Construct Retaining Walls	128 days	Tue 6/13/23	Mon 12/11/23												
57	(Sub) Tri-State Curb Placing Remainder of Sidewalks up to STA 108+50	7 days	Fri 6/2/23	Mon 6/12/23												
58	Backing Sidewalks Fine Grading/Loaming/Seeding STA 101+50 to STA 108+50	7 days	Wed 6/14/23	Thu 6/22/23												
59	E.D. Swett Constructing Abutment B Pile Cap	30 days	Wed 6/21/23	Wed 8/2/23												
60	WATER Testing In Preperation for Service Install	5 days	Wed 6/21/23	Tue 6/27/23												
61	WATER Tie-In New and Exsting 8" Water Line Services on Pearl Street and Winchester Street	3 days	Wed 6/28/23	Fri 6/30/23												
62	WATER Install New 3/4" Poly Water Line Services 2-Pearl Street 2-Island Street 1-Island Street Roundabout	4 days	Mon 7/3/23	Fri 7/7/23												
63	DRAINAGE Install 42LF 24" HDPE from CB#27 (114+25 RT 45) to CB#31 (114+25 LT 42) Install CB#31	2 days	Mon 7/10/23	Tue 7/11/23												
64	DRAINAGE Install 61LF 18" HDPE From CB#31 (114+25 LT 42) to CB#30 (400+85 RT 2) Install CB#30	2 days	Wed 7/12/23	Thu 7/13/23												
65	E.D. Swett Construct Abutment A Pile Cap	28 days	Wed 7/12/23	Fri 8/18/23												
66	Box Cut Pearl Street and Island Street Intersection	7 days	Fri 6/23/23	Mon 7/3/23												
67	DRAINAGE Install 19LF of 18" HDPE From CB#30 (400+85 RT 2) to CB#29 (114+92 LT 88) Install CB#29	1 day	Fri 7/14/23	Fri 7/14/23												
68	DRAINAGE Remove Existing RCP Pipe from CB#29 to Purposed MH#49 Remove Existing CB at Purposed MH#49 Install 36LF of 15" HDPE from CB#29 to MH#49 Connect 8" CI into MH#49	2 days	Mon 7/17/23	Tue 7/18/23												
69	DRAINAGE Install 66LF of 15" HDPE From MH#49 (401+18 RT 17) to CB #28 (401+83 RT 14) Install CB#28 Remove Existing CB Located By CB#28	3 days	Wed 7/19/23	Fri 7/21/23												

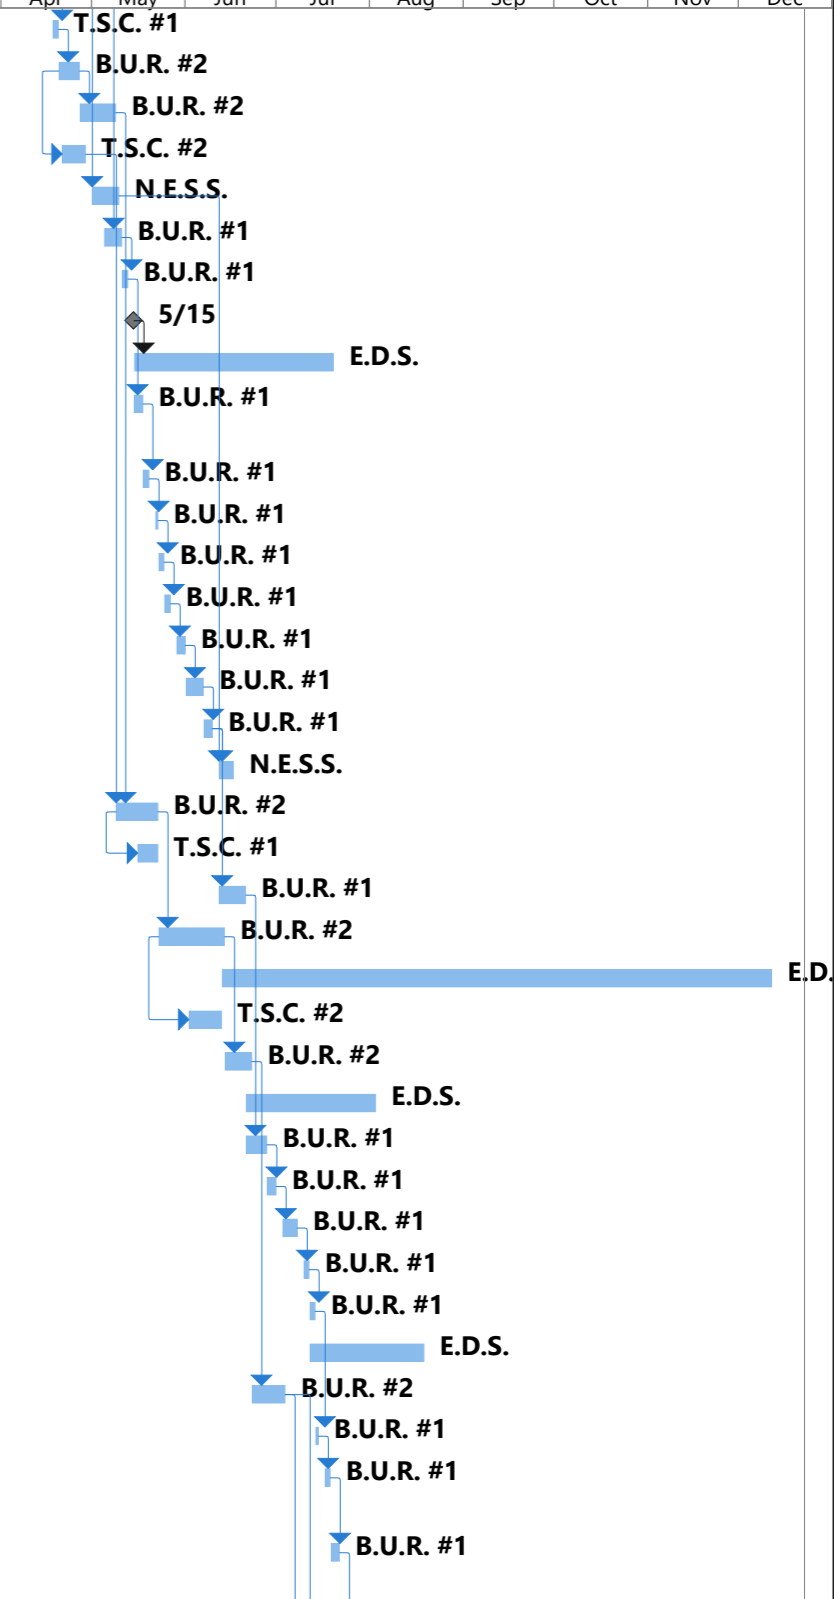

Project: Keene, NH Winchester
Date: Wed 3/22/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
70	DRAINAGE Remove Existing CB Located Between CB#29 and CB#1 Install 47LF of 15" HDPE from CB#29 (114+92 LT 88) to CB#1 ((500+95 LT 34) Install CB#1	2 days	Mon 7/24/23	Tue 7/25/23								B.U.R. #1				
71	DRAINAGE Install 66LF of 15" HDPE from CB#1 (500+95 LT 34) to CB#2 (501+26 RT 23) Install CB#2	2 days	Wed 7/26/23	Thu 7/27/23								B.U.R. #1				
72	DRAINAGE Remove Existing Structures #1390, 1244 and 1256. Remove Existing MH Fill and Abandon Existing Pipes 2.7CY	1 day	Fri 7/28/23	Fri 7/28/23								B.U.R. #1				
73	DRAINAGE Install 41LF of 15" HDPE from Vegetation Treatment Swale to CB#4 (116+90 LT 23.8) Install CB#4	2 days	Mon 7/31/23	Tue 8/1/23								B.U.R. #1				
74	DRAINAGE Install 113LF of 15" HDPE from CB#4 (116+90 LT 23.8) to CB#3 (115+67 LT 58.9) Install CB #3	3 days	Wed 8/2/23	Fri 8/4/23								B.U.R. #1				
75	DRAINAGE Install 60LF 15" HDPE from CB#3 (115+67 LT 58.9) to CB#33 (115+77) Install CB#33	2 days	Mon 8/7/23	Tue 8/8/23								B.U.R. #1				
76	Install Electrical Service For Island Street Roundabout	1 day	Wed 8/9/23	Wed 8/9/23								B.U.R. #1				
77	Retaining Wall Construction by Keene State Parking Lot	9 days	Thu 8/10/23	Tue 8/22/23								B.U.R. #1				
78	E.D. Swett Structural Steel	8 days	Mon 8/21/23	Wed 8/30/23												
79	B.U.R. 2 Float	5 days	Wed 7/5/23	Tue 7/11/23								B.U.R. #2				
80	(Sub) All State Reclaim STA 108+50 to Island Street	3 days	Fri 7/7/23	Tue 7/11/23								A.S.A.				
81	Winchester Street Road Grading STA 108+50 to Island Street	5 days	Wed 7/12/23	Tue 7/18/23								B.U.R. #2				
82	(Sub) All State Paving Base and Binder Courses STA 108+50 to Island Street	4 days	Wed 7/19/23	Mon 7/24/23								A.S.A.				
83	New Traffic Pattern Switch to Phase 4	1 day	Mon 7/24/23	Tue 7/25/23								B.U.R.				
84	Raise Structures to Finish Grade	7 days	Wed 8/23/23	Thu 8/31/23											B.U.R. #1	
85	Install Bioretention Median	5 days	Tue 7/25/23	Mon 7/31/23								B.U.R. #2				
86	(Sub) Tri-State Curb Granite Curb Install Island Street Roundabout Inner/Outer Circle, STA 108+50 to 1350+00 ¹¹³⁺⁵⁰ RT and LT Sides, Keene Sate Parking Exit	5 days	Tue 7/25/23	Mon 7/31/23								T.S.C. #1				
87	Grading For Island Street Roundabout Winchester Street Sidewalk Grading 108+50 to 1350+00 ¹¹³⁺⁵⁰	10 days	Tue 8/1/23	Mon 8/14/23								B.U.R. #2				
88	(Sub) Tri-State Place Island Street Roundabout and Winchester Street Sidewalks 108+50 to 1350+00 ¹¹³⁺⁵⁰ RT and LT Sides	5 days	Tue 8/15/23	Mon 8/21/23								T.S.C. #2				
89	Remove Existing Sidewalk and Curb Island Street And Pearl Street	5 days	Tue 8/15/23	Mon 8/21/23								B.U.R. #2				
90	B.U.R. 2 Float	5 days	Tue 8/22/23	Mon 8/28/23								B.U.R. #2				
91	E.D. Swett Construct Concrete Bridge Deck	72 days	Thu 8/31/23	Mon 12/11/23												
92	Backing Sidewalks Fine Grading/Loaming To STA 108+50 to 1350+00 ¹¹³⁺⁵⁰	5 days	Tue 8/29/23	Mon 9/4/23								B.U.R. #2				
93	(Sub) Vermont Rec Installing Retaining Wall Fence By Keene State Parking Lot	3 days	Wed 9/6/23	Fri 9/8/23								V.R.				
94	(Sub) Tri-State Curb Install All Remaining Curb Win, Pearl, Island.	5 days	Wed 9/6/23	Tue 9/12/23								T.S.C. #1				
95	Grading For Remaining Sidewalk On Win, Pearl, Island	8 days	Thu 8/31/23	Sun 9/3/23								B.U.R.				
96	(Sub) Garwall Plantings Riverside/Island Street Roundabouts	2 days	Wed 9/13/23	Thu 9/14/23								GW				
97	(Sub) Tri-State Curb Placing Remaining Sidewalks on Win, Pear, Island	4 days	Mon 9/4/23	Fri 9/8/23								T.S.C. #2				
98	BUR Foat	4 days	Mon 9/4/23	Fri 9/8/23								B.U.R.				
99	Backing Sidewalk Final Grading/Loaming	5 days	Fri 9/8/23	Sun 9/10/23								B.U.R.				
100	(Sub) All State Paving Final Top Course (Excluding Island Street Bridge Approaches)	4 days	Mon 9/11/23	Thu 9/14/23								A.S.A.				
101	(Sub) A.F.T.C. Final Project Signage	5 days	Fri 9/15/23	Thu 9/21/23								A.T.F.C.				
102	(Sub) L&D Final Stripping	3 days	Fri 9/22/23	Tue 9/26/23								L&D				
103	Project Punch List - Demob	30 days	Mon 9/11/23	Fri 10/20/23											B.U.R.	
104	E.D. Swett Abutment A Deck End	12 days	Thu 9/28/23	Fri 10/13/23											E.D.S.	
105	E.D. Swett Abutment B Deck End	13 days	Thu 9/28/23	Mon 10/16/23											E.D.S.	

Project: Keene, NH Winchester
Date: Wed 3/22/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
106	E.D. Swett Abutment A Approach Slab	26 days	Mon 10/16/23	Mon 11/20/23												E.D.S.
107	E.D. Swett Sleeper Slab	10 days	Mon 10/23/23	Fri 11/3/23												E.D.S.
108	E.D. Swett Sleeper Slab Header	10 days	Mon 10/30/23	Fri 11/10/23												E.D.S.
109	E.D. Swett Approach Slab	10 days	Tue 11/7/23	Mon 11/20/23												E.D.S.
110	E.D. Swett Abutment B Approach Slab	35 days	Tue 10/17/23	Mon 12/4/23												E.D.S.
111	E.D. Swett Sleeper Slab	10 days	Mon 11/6/23	Fri 11/17/23												E.D.S.
112	E.D. Swett Sleeper Slab Header	10 days	Mon 11/13/23	Fri 11/24/23												E.D.S.
113	E.D. Swett Approach Slab	10 days	Tue 11/21/23	Mon 12/4/23												E.D.S.
114	E.D. Swett Construct Upstream Sidewalk	10 days	Tue 11/28/23	Mon 12/11/23												E.D.
115	E.D. Swett Construct Downstream Sidewalk	11 days	Tue 11/28/23	Tue 12/12/23												E.D.
116	E.D. Swett Open Island Street Bridge	1 day	Fri 12/22/23	Fri 12/22/23												E.
117			Thu 1/26/23													
118		1 day	Thu 1/26/23	Thu 1/26/23												
119	SEWER Change Order Work SMH#7 SMH#8 and 63LF of Connecting Pipe	3 days	Thu 1/26/23	Mon 1/30/23												
120	DRAINAGE Change Order Work Install CB #54 and 107LF of 24" HDPE	2 days	Thu 1/26/23	Fri 1/27/23												
121	All State Paving Island Street Bridge Approaches	1 day	Thu 1/26/23	Thu 1/26/23												

Project: Keene, NH Winchester Date: Wed 3/22/23	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
